

PLAN DE TRABAJO

METROBUS RUTA 8 - TRES DE FEBRERO

MINISTERIO DE TRANSPORTE - SECRETARIA DE OBRAS DE TRANSPORTE



Ministerio de Transporte
Presidencia de la Nación



ITEM	DESCRIPCION	SUBTOTAL	%	DIAS							
				abr-17	may-17	jun-17	jul-17	ago-17	30-sep	07-oct	
1	TRABAJOS PRELIMINARES	\$ 6.426.850,90	5,30%	6,00%	6,00%	12,00%	25,00%	25,00%	26,00%		
2	MOVIMIENTO DE TIERRA / DEMOLICIONES	\$ 2.965.005,20	2,44%			10,00%	30,00%	48,00%	12,00%		
3	DE HORMIGON ARMADO	\$ 22.754.679,53	18,76%		5,00%	25,00%	25,00%	30,00%	15,00%		
4	ESTRUCTURA METALICA	\$ 17.514.544,39	14,44%				30,00%	35,00%	35,00%		
5	CUBIERTA	\$ 5.823.964,81	4,80%				20,00%	50,00%	29,50%	0,50%	
6	INSTALACION ELECTRICA	\$ 10.861.146,15	8,96%				25,00%	45,00%	30,00%		
7	PISOS Y PAVIMENTOS	\$ 4.661.342,50	3,84%				30,00%	45,00%	25,00%		
8	CARPINTERIA METALICA	\$ 6.336.698,96	5,22%				20,00%	55,00%	8,00%	17,00%	
9	VIDRIOS	\$ 6.459.577,92	5,33%					25,00%	75,00%		
10	EQUIPAMIENTO	\$ 1.749.100,34	1,44%					25,00%	49,00%	26,00%	
11	EQUIPAMIENTO Y SEGURIDAD VIAL	\$ 10.046.389,14	8,28%					20,00%	46,00%	34,00%	
12	CANTEROS PREMOLDEADOS	\$ 12.796.737,19	10,55%					70,00%	27,95%	2,05%	
13	VEGETACION	\$ 8.633.622,56	7,12%					30,00%	44,00%	26,00%	
14	GRAFICA	\$ 346.331,34	0,29%					20,00%	80,00%		
15	VARIOS	\$ 3.901.878,68	3,22%	6,00%	6,00%	12,00%	25,00%	25,00%	25,00%	1,00%	
TOTAL		\$ 121.277.869,61	100,00%								
AVANCE PARCIAL EN PORCENTAJE				0,51%	1,45%	5,96%	17,28%	37,95%	30,65%	6,20%	
AVANCE ACUMULADO PORCENTUAL				0,51%	1,96%	7,92%	25,20%	63,15%	93,80%	100,00%	
AVANCE PARCIAL EN PORCENTAJE				0,51%	2,01%	3,30%	10,11%	11,24%	68,39%	4,45%	
AVANCE ACUMULADO PORCENTUAL				0,51%	2,52%	5,81%	15,92%	27,16%	95,55%	100,00%	
PLAN DE CERTIFICACION EN PESOS				\$ 619.723,77	\$ 1.757.457,75	\$ 7.224.617,95	\$ 20.960.539,20	\$ 46.022.682,47	\$ 37.169.857,65	\$ 7.522.990,81	
PLAN DE CERTIFICACION EN PESOS				\$ 619.723,77	\$ 2.377.181,53	\$ 9.601.799,48	\$ 30.562.338,68	\$ 76.585.021,15	\$ 113.754.878,80	\$ 121.277.869,61	
PLAN DE CERTIFICACION EN PESOS				\$ 618.116,43	\$ 2.435.815,79	\$ 3.997.327,01	\$ 12.260.158,19	\$ 13.626.824,39	\$ 82.938.709,12	\$ 5.400.918,67	
PLAN DE CERTIFICACION EN PESOS				\$ 618.116,43	\$ 3.053.932,22	\$ 7.051.259,23	\$ 19.311.417,42	\$ 32.938.241,81	\$ 115.876.950,93	\$ 121.277.869,60	


NOTA:

Curva de Inversión y Plan de Trabajo Aprobado por Dirección de Obra

BRICONS S.A.I.C.F.I.

Arq. JORGE D. RASPAGLIESI

AVANCE REAL VS CONTRATO

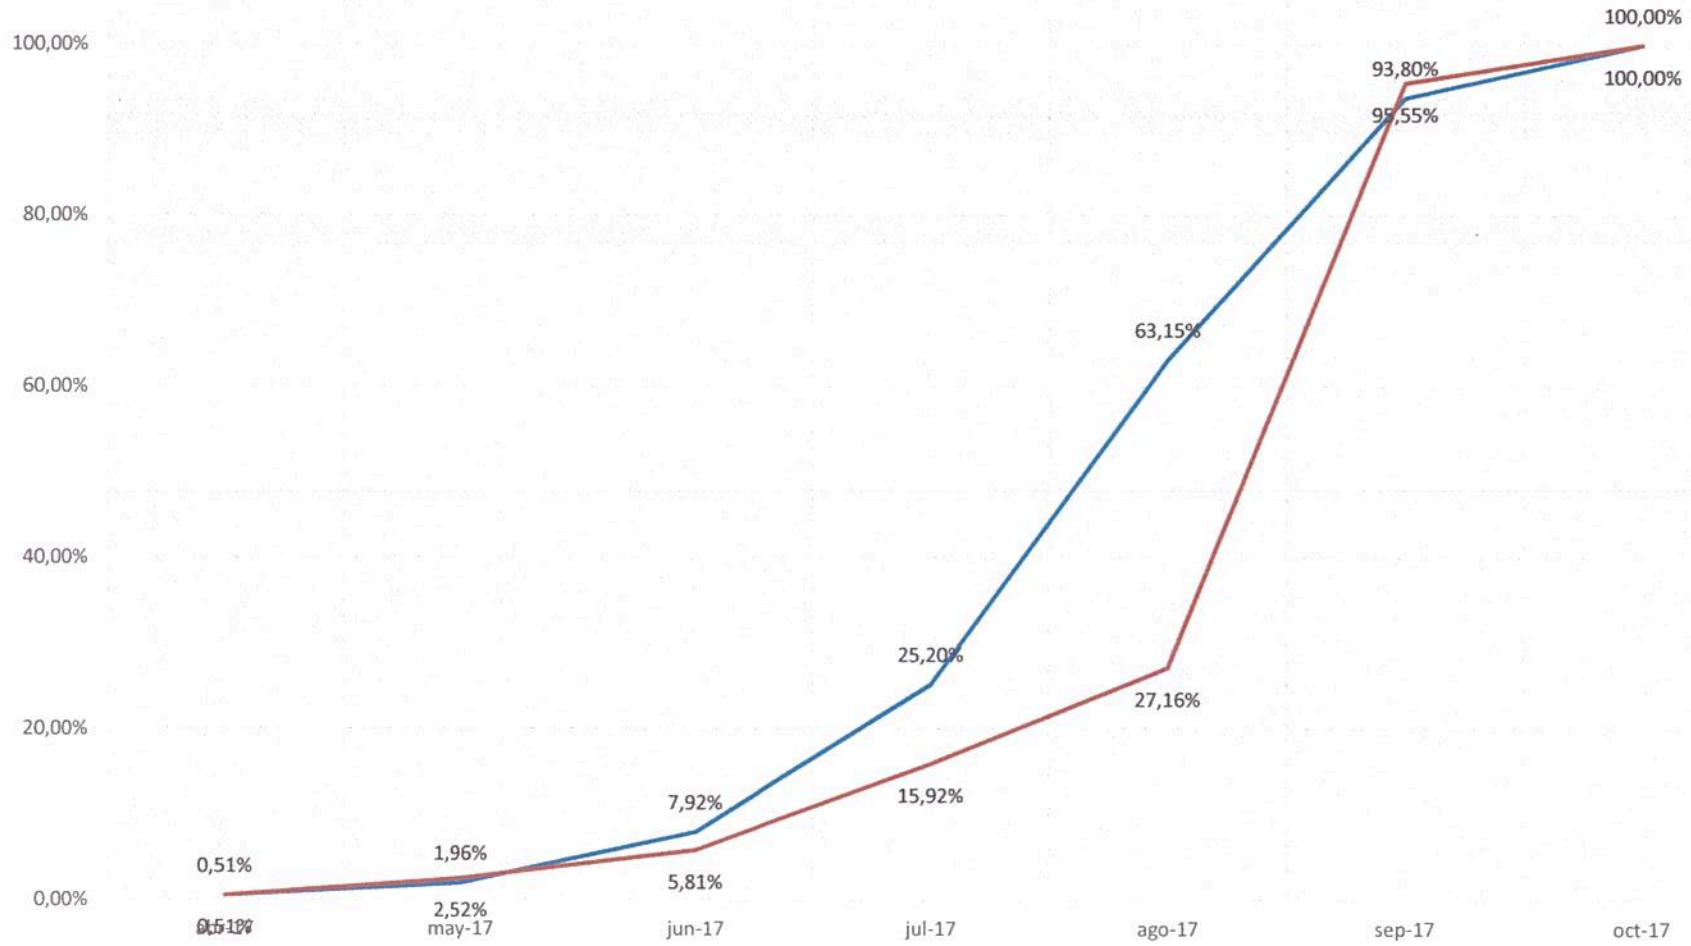

BRICONS S.A.I.C.F.I.
Arq. JORGE D. RASPAGLIESI
REPRESENTANTE TECNICO
